



# Holland Patent CSD 2023 Capital Project Phase 1 Update

April 14, 2025

# Completed Work –Middle School Tech Shop Improvements

- Polished Concrete Floors/New Ceilings/Lighting Upgrades/New Casework/HVAC Upgrades



# Completed Work – New Hot Water Heaters in Middle School Boiler Room

- Removed Old Hot Water Heaters in Boiler Room and Installed Two New Ones






# Work in Progress – Middle School Computer Classroom

- New Red Oak Parquet Flooring and Base (Expected Completion End of April 2025)



# Work in Progress – Middle School Art Suite

- Complete Renovation of Existing Art Room and Faculty Room to Make New Art Suite (Expected Completion May 2025)
- New Floors/Ceilings/Ceramic Wall Tile/Kiln Room/Casework/Sinks/Mechanical Units/Electrical Upgrades

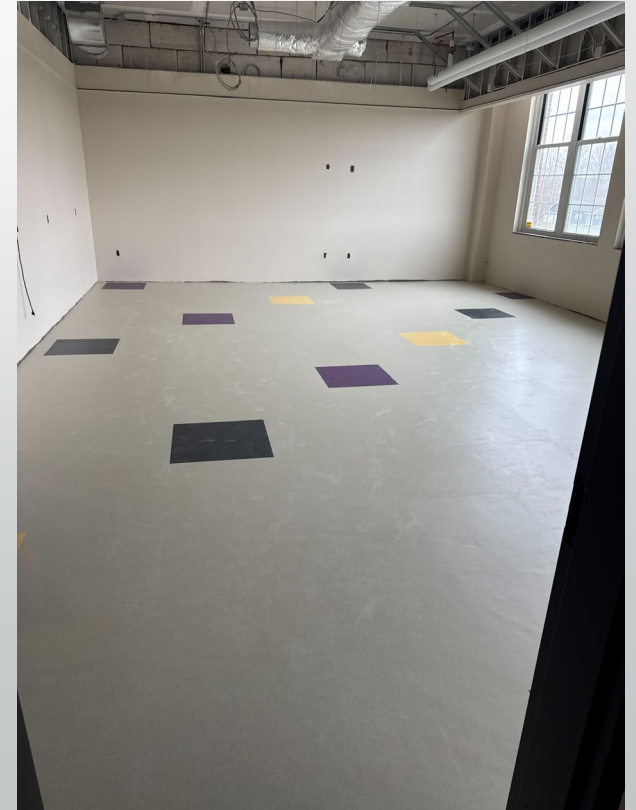



# Work in Progress – Middle School Principal Office/Assistant Principal Office/Faculty Room

- New Ceilings/Light Fixtures/Paint/Mechanical Units/Electrical Upgrades (Expected Completion Beginning of May 2025)





# Work in Progress – High School Field

- New Turf Multi-Purpose Field/Stadium Lighting/Drainage Improvements/Bleachers/Video Scoreboard/Marking Lot/Sidewalks (Expected Completion September 2025)



# Work Left to Begin

- New Carpet in Middle School Vocal Music Room (Beginning 4/18/25)
- New Electrical Service Upgrades at the High School (Summer 2025)
